Physical Resources Committee

Wednesday, September 3, 2025 – 1:30 p.m. Zoom Meeting: https://rsccd-edu.zoom.us/j/84726781298

Agenda

- 1. Call to Order Ingram
- 2. Introductions Ingram
- 3. Approval of Meeting Minutes May 7, 2025 (Action) Ingram
- 4. Physical Resources Committee Purpose and Responsibilities (Action) Ingram
- 5. Physical Resources Committee Membership (Action) Ingram
- 6. Projects Update Matsumoto
 - 24-25 Fiscal Year in Review Snapshot
 - Capital Projects
 - Scheduled Maintenance Projects
 - Facility Modification Requests
 - ADA Transition Plan and Blaser Settlement
 - Districtwide Access Control and Key Test Pilot Projects
 - Districtwide Unfunded Projects
 - State Chancellor's Office Deadlines
 - Real Estate and Capital Planning
 - Energy and Sustainability

Sustainable RSCCD (SRC) Next Meeting September 18, 2024 - Website: https://www.rsccd.edu/Departments/BusinessServices/sustainable-rsccd-committee/Pages/default.aspx

- 7. Update on Campus Facilities Meetings
 - SAC Facilities and Safety Committee Update Hoffman
 - Next Meeting September 16, 2025
 - SCC Facilities and Safety Committee Update Satele
 - Next Meeting September 15, 2025
- 8. Meeting Schedule 2025-26: September 3, 2025; October 1, 2025 (Email only); November 12, 2025*, February 4, 2026 (Email only); March 4, 2026, and May 6, 2026 * Meeting date changed due to conflict with CCFC conference
- 9. Other
- 10. Adjournment

The Rancho Santiago Community College District aspires to provide equitable, exemplary educational programs and services in safe, inclusive, and supportive learning environments that empower our diverse students and communities to achieve their personal, professional, and academic goals.

Physical Resources Committee Minutes of May 7, 2025

Members Present: Iris Ingram, Carri Matsumoto, Darlene Diaz, Dane Clacken, Suzanne Freeman, Bart Hoffman, Bridgette Hernandez, Tamara Mahdi, Joe Melendez, and Arleen Satele

Members Absent: Michael Busch, Christine Gascon, Jennifer Karimpour, Shannon Kaveney, Cristina Morones, Raelyssa Sanchez, and Michael Turrentine

Guests Present: Alejandro Alcala, Hugo Curiel, Tae Kim, Kelvin Leeds, and Kennethia Vega (recorder)

1. Call To Order

Ingram welcomed everyone to the meeting and called the meeting to order upon achieving quorum at 1:32 pm.

2. <u>Introductions:</u>

Introductions were completed.

- 3. Approval of Meeting Minutes March 5, 2025 (Action)
 - A motion made by Matsumoto to approve the minutes of March 5, 2025, meeting as presented was seconded by Clacken. By roll call vote the motion passed unanimously.
- 4. <u>Capital Construction Needs Financing Options for CEC and OEC Projects</u> Ingram Ingram advised she will present clarifying information to the Board of Trustees on May 12 as a secondary follow-up to previous presentations on how to finance future capital needs, primarily for CEC and OEC since RSCCD was not successful in obtaining a general obligation bond. The plan is for \$150 million divided between the two sites. She explained it is a combination of borrowing through a certificate of participation program and use of the reserves. It is the Board's decision to pursue these funds through such strategies. There were no questions.
- 5. <u>Projects Update</u> (Matsumoto)

Matsumoto screenshared the projects update now organized by subsections as follows:

- Capital Projects
- Scheduled Maintenance Projects
- Facility Modification Requests
- ADA Transition Plan & Blaser Settlement
- Districtwide Access Control & Key Test Pilot Projects
- Districtwide Unfunded Projects
- State Chancellor's Office Deadlines
- Sustainable Master Plan Update

All updates/revisions are in **blue text** and the presentation is posted on the PRC webpage for ease of review, reference, and sharing with constituents.

A highlight of Capital and construction projects include:

- Closeout of Russell Hall Demolition is nearing the end. It will come off the project list once completely off the books and all bills paid.
- SAC Entrance Improvement Project is running a bit behind schedule.
 Melendez noted high voltage work will commence over a weekend and will
 affect other buildings including H and E; communication will be distributed
 to advise and alert the campus. The effort is being coordinated through M
 & O department. Discussion ensued about SAC also sending out
 construction alerts to keep campus community informed.
- Included in the project update are the planning studies for both CEC and OEC that occurred over the last year or so. OEC Site remediation is still in progress and going well.
- Still searching for replacement of Chapman site as the lease will end in December
- SCC Campus Entrance Improvement Phase 2 bid was awarded, and work will begin that will impact the front entrance to the SCC campus in June and July before the fall semester starts. Matsumoto explained the need for the work because of the Blaser Settlement providing accessible path of travel from the public right of way up to the main entrance of the campus.
- Scheduled Maintenance projects were referenced and updates provided.
- Five-Year Capital Outlay Plan is due to the CCCCO on July 1, 2025. This document provides the State with an idea of what the colleges plan for the future.
- Sustainability Plan is complete and will be shared with the Board Facilities Committee on May 20 and the Board of Trustees on May 27.
- Discussion ensued about the Criminal Justice Academy using Fusion for scheduling classes. Staff are available to train to assist with the requirements of it becoming a new center. Hoffman, Matsumoto, ITS, and Educational Services can meet to discuss the matter in complete detail.

6. Sustainability Committee Update

Matsumoto noted the next Sustainability Committee meeting is May 21, 2025. Hoffman and Satele provided brief reports on the Earth Day events at the respective sites.

7. Update to Campus Facilities

- SAC Hoffman reported on the activities of the last facilities meeting on April 15, 2025, with the workgroup focusing on the unhoused and homeless on the campus. District staff also provided updates.
- SCC Satele reported on the activities of the last facilities meeting in April
 commenting on presentation by district staff on the front entrance project that
 will have major impact to the campus.

8. Meeting Schedule for 2025-26

A motion by Satele to approve the meeting schedule as presented was seconded by Hoffman. By roll call vote the motion passed unanimously.

9. Other

There were no further questions or concerns expressed.

10. Adjournment

A motion made by Hoffman was seconded by Clacken to adjourn the meeting. The meeting adjourned at 2:18 pm.

Physical Resources Committee Meeting Wednesday, September 3, 2025

Purpose: The Physical Resources Committee supports the district and colleges by coordinating and overseeing capital outlay construction and scheduled maintenance projects that align with the facilities master plans to provide for a safe and sustainable environment and to protect district property.

Responsibilities: Review plans related to district and college physical resources including facilities, equipment, land and other assets. Assess the effective use of physical resources. Review the following:

- Five-Year State Annual Capital Construction Plan
- State Capital Outlay projects
- Local bond projects
- Five-Year Annual State Scheduled Maintenance Plan
- Facility Master Plans
- Hazardous Mitigation Plans as needed
- Ancillary costs related to new construction as needed

Physical Resources Committee Membership as of August 2025			
Santa Ana College	Santiago Canyon College	District Office	
Bart Hoffman (Vice President, Administrative Services)	Arleen Satele (Vice President, Administrative Services)	Iris I. Ingram (Vice Chancellor, Business Services) – Co-Chair	
Shannon Kaveney (Management)	Christine Gascon (Management)	Carri Matsumoto (Asst. Vice Chancellor, Facility Planning)	
Michael Busch (Faculty)	Darlene Diaz (Faculty)	Joe Melendez (Director, Facility Planning)	
Suzanne Freeman (Faculty)	Cristina Morones (Faculty)	Dane Clacken (Management)	
Michael Turrentine (CSEA)	Jennifer Karimpour (CSEA)	Bridgette Hernandez, Co-Chair (CSEA)	
Vacant (Student)	Isabella Luna (Student)		

Membership Notes:

- One of the classified representatives shall serve as committee co-chair
- Three classified representatives appointed by CSEA (District Office, Santa Ana College and Santiago Canyon College)
- Management representatives, appointed by each College President and Vice Chancellor, Business Services
- Two faculty members, appointed by each Academic Senate, Santa Ana College and Santiago Canyon College
- Student representatives (Santa Ana College and Santiago Canyon College, when possible)



Table of Contents

- 24-25 Fiscal Year in Review Snapshot
- Capital Projects
- Scheduled Maintenance Projects
- Facility Modification Requests
- ADA Transition Plan and Blaser Settlement
- Districtwide Access Control and Key Test Pilot Projects
- Districtwide Unfunded Projects
- State Chancellor's Office Deadlines
- Real Estate and Capital Planning
- Energy and Sustainability



Fiscal Year in Review (24-25) as of June 30, 2025

Activity/Category	Active/In Progress	Completed/ Closed	Total
Capital Projects	60	12	72
Scheduled Maintenance	20	8	28
College Facility Modification Requests (FMRs)	45	38	83
Total	125	58	183
Fire Life Safety Projects	18	-	-
Real Estate & Planning	22	-	-
Energy & Sustainability	7	-	-
Public Records Act Requests	99	40	139
Bids	5	79	84
Contracts & Amendments	5	123	128
RFQs/RFPs	3	27	30
Invoices Processed	75	878	953

Capital Projects



Current Capital Projects Russell Hall Replacement (Health Sciences Building) Santa Ana College

Project Summary:

- Construction of a new 55,563 square foot Health Sciences Building to include Nursing, Occupational Therapy Assistant, Emergency Medical Technician, Pharmacy Technology, and 20 general classrooms and computer labs. New building will be located south of the existing library and north of the new Science Center
- Demolition of existing Russell Hall Building

Current Status:

- Notice of Completion approved by the Board of Trustees on December 11, 2023.
- The College held a Grand Opening event on January 10, 2024.
- In close-out.

Budget:

- \$58.8 million (budget under review) includes demo budget. Working on final close-out report.
- \$20,729,000 state funded (2023 estimated contribution) includes demo budget.





Current Capital Projects Russell Hall Demolition Santa Ana College

Project Summary:

Demolition of existing Russell Hall Building

Current Status:

- Notice of Completion was approved by the Board of Trustees on November 13, 2024.
- The State Chancellor's Office approved additional allocation of funds.
- ▶ In close-out.

Budget:

- \$2.5 million. Working on final close-out report.
- \$1,697,000 state funded (2023 estimated contribution)





Project Summary:


- Campus Entrance Improvement project Phase 1 is scheduled to start upon completion of Russell Hall Demolition project anticipated October 2024. Project objectives include traffic congestion reduction, improve pedestrian and vehicle circulation, remove accessibility barriers, increase bus/ride-share drop-offs, and improve the campus front entry.
- In an effort to minimize college impacts and provide flexible construction budget options, project will be phased into three (3) phases.
- Phase 1: front entry renovations, softscape and hardscape improvements, introduction of a new "hairpin" vehicular turn, shade structure and front entry plaza improvements.
- Phase 2: Parking Lot # 1 renovations with hardscape and softscape improvements and increased parking stalls counts.
- Phase 3: Parking Lot # 3 and # 4 renovations with hardscape and softscape improvements, increased parking stall counts, increased drop-off areas, and dedicated ride-sharing areas.
- All phases will improve traffic and pedestrian circulation & safety and remove accessibility barriers.


Current Status:

Concrete finish work, landscape, lighting, and furnishing installations in progress.


Budget:

\$5.5 million








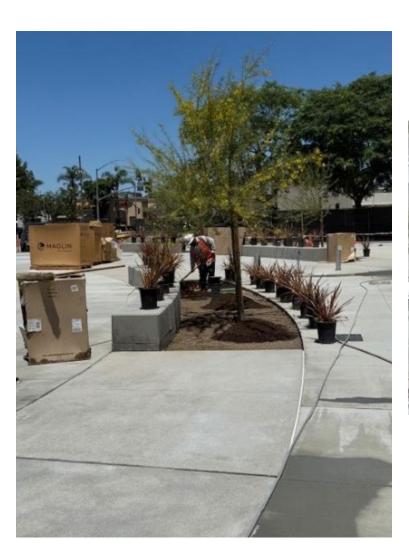




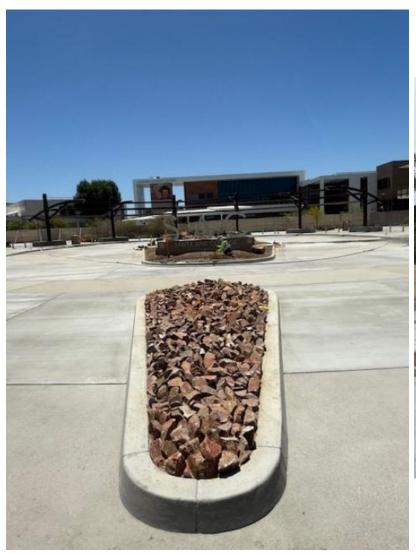






Current Capital Projects Construction Logistics Plan Alternate Campus Entrances & Vehicular Routes

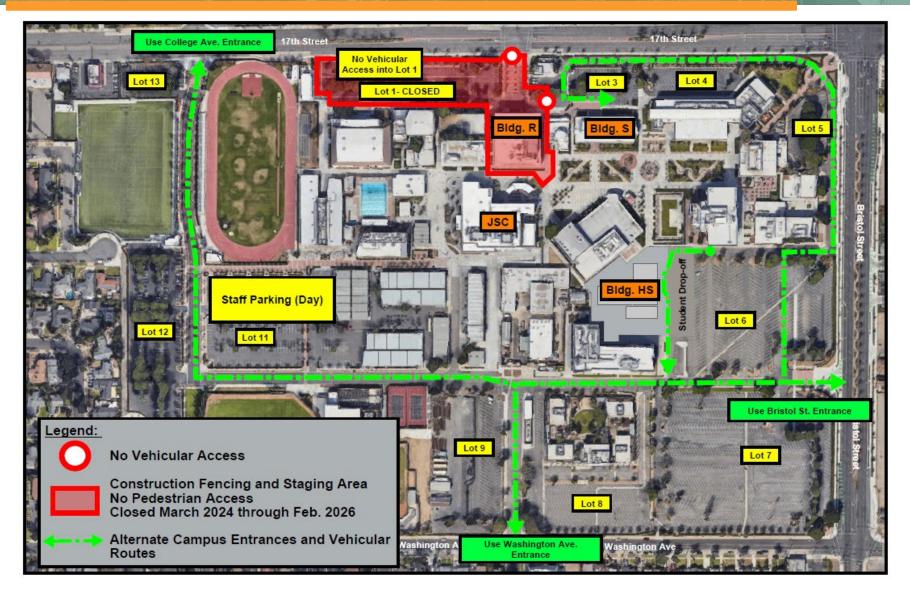

Current Capital Projects Construction Logistics Plan Pedestrian Paths of Travel



Current Capital Projects Construction Logistics Plan ADA Parking Path of Travel

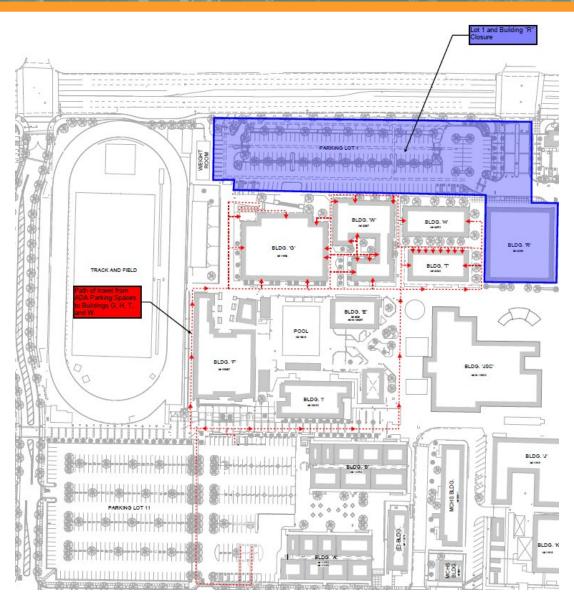

Current Capital Projects Secondary Projects Santa Ana College

Project	Status	Expended Amount
Health Sciences Building Secondary Projects	Completed close-out. This project will be removed from future updates.	\$214,678



Current Capital Projects Reconfigurations & Restoration Santa Ana College

Project	Status	Estimated Budget
Temporary Village (TV) Phase 5A Fashion & Others	All program relocations have been finalized including: the El Don Media program, the Thrive Center and the Fashion and Merchandising program. The notice of completion is anticipated for approval by the Board of Trustees on September 15, 2025.	\$1,633,466





Current Capital Projects Santa Ana College

Project	Status	Estimated Budget
DW ITS Center Reconfiguration	Design development phase completed. To be presented at upcoming Facilities and Safety Committee Meeting.	\$3,999,000
Stormwater Management Site Improvements	Close-out phase.	\$315,873



Current Capital Projects Centennial Education Center Redevelopment Santa Ana College

Project Summary:

- ► The Centennial Education Center (CEC) was built in 1980
- Located at 2900 W. Edinger Avenue in the City of Santa Ana
- 80-year lease with City of Santa Ana May 8, 2020 June 3, 2101 (supersedes prior agreement from 1979)
- New lease requires significant improvements
- The existing campus is comprised of seven modular buildings of approximately 48,157 gsf and is currently located within a leased site boundary of approximately 109,000 sf in Centennial Park
- ▶ The CEC Replacement project considers a new 77,135 gsf campus facility

Current Status:

- Several meetings have occurred with President's Cabinet, work and user groups.
- Development scenarios being studied.
- New architect agreement given change in scope was approved by the Board of trustees on August 11, 2025.

Budget:


- Planning Only \$908,365 (under review)
- \$1 Million Improvement Contribution



Current Capital Projects Existing Centennial Education Center Site Santa Ana College



Current Capital Projects Centennial Education Center - Renovation Plan Santa Ana College

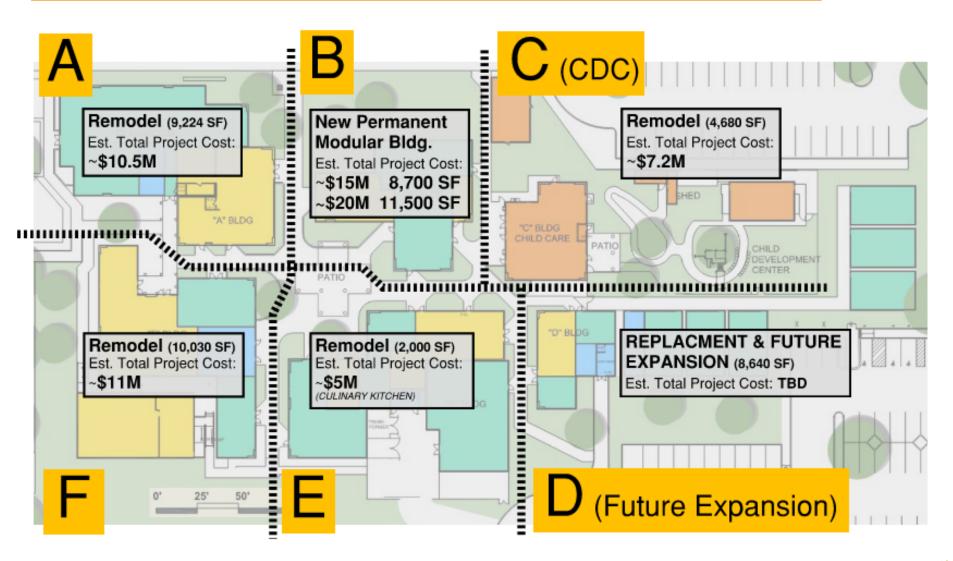

Current Capital Projects Centennial Education Center - Project Development Status Santa Ana College

- College has identified the scopes of work:
 - Building B replacement
 - Culinary Kitchen in Building E, partial modernization
 - ► Capital Contribution (\$1 million) adjacent lease boundary site improvements
- Meetings with City of Santa Ana to discuss new proposed scope of work for project and lease amendment.
- MRY Architects contract BOT approval 8/11/25 on revised scope of work for 3 phases plus assessment of future phases



Current Capital Projects Centennial Education Center - Project Planning Budgets Santa Ana College

A. Phase 1 Replace Building B	B. Culinary Kitchen Building E Modernization	C. Capital Contribution Improvements	D. Future Phases
\$15-\$20 million (8,700 SF - 11,500 SF) (30+ months)	\$5 million (subject to change depending on DSA review) (20+ months)	\$1 million (subject to change depending on scope of work to be decided upon with City) (28+ months)	TBD depending on funding remaining.

Budgets may change depending upon site work and DSA requirements which are unknown at this time. CEC budget allocated is currently approximately \$4.6M which covers architect design fees for A, B and C.

Current Capital Projects Centennial Education Center - Phase 1 Santa Ana College

Administrative / Student Services Building

- New permanent modular building ~ 8,700 - 11,500 SF
 - Private offices
 - Open offices
 - Meeting spaces
- New courtyard / exterior site improvements
- Total site improvements ~ 20,500 SF
- Demolish existing Building B



CEC PHASE 1: 30+ months




Current Capital Projects Centennial Education Center - Culinary Kitchen Santa Ana College

Remodel Portion of Bldg. E ~ 1,500 SF

- ~1,351 sf laboratory/classroom
- ~145 sf warewashing area
- Exterior site/utility improvements
- Function as classroom/laboratory
 - Fundamental skills of food preparation; kitchen organization; basic cooking and baking techniques; professional standards used in modern commercial kitchens



Kitchen Preliminary Study



Current Capital Projects Centennial Education Center - Capital Contribution Improvements Santa Ana College

District one-time Capital Contribution to Centennial Park (\$1M)

- Per ground lease of May 8, 2020, with City of Santa Ana, improvements shall be agreed upon by both parties
- Potential improvements shall be adjacent lease boundary and may include:
 - Concrete pathway
 - Exterior lighting
 - Landscape improvements
 - Outdoor area for events/gatherings



CEC IMPROVEMENTS (\$1M): 28+ months

DESIGN 7-8 mo.

CEQA (NOE/ND) 4-6 mo. DSA PLAN CHECK 6 mo.

BID 3 mo. CONSTRUCTION 12-16 mo.

Current Capital Projects Orange Education Center Site Remediation Santiago Canyon College

Project Summary:

- While undertaking a redevelopment design option to upgrade building to meet DSA building code standards, underground soil vapor contamination was discovered. Historical data revealed existing building resided on a site that was previously used for industrial business use.
- As a result of newer environmental regulations and to meet Orange County Health Department requirements for commercial clean-up standards, building was demolished March 2020 in order to clean up soil vapors on the property.
- The District and College are exploring options of potential development of the 'non-impacted' area of the site that occur within a target budget of available funds.

Current Status:

- On-going site remediation is underway.
- 2025 Q2 Report was submitted to OCHCA.
- Exploring various development options.

Budget: Under Review

\$25 million remaining in Budget

Incurring ongoing remediation and interim housing lease costs







Current Capital Projects Orange Education Center Development Options

- Lease
- New Property Acquisition
- Redevelop Batavia



Current Capital Projects Orange Education Center Current Leased Sites

Need to relocate Chapman Center due to property being sold and lease expiring.

	CHAPMAN CENTER 1937 W. Chapman Ave., Suite 200 Orange, CA 92868	MAIN (CWPC) 1572 N. Main St., Orange, CA 92867
Lease End Date	1/31/2026	1/31/2028
SF	~12,913	~8,400
Classrooms	8	4
Administrative/Offices	yes	yes
Parking	~100*	~50*




^{*} PARKING IS LIMITED

Current Capital Projects Orange Education Center Site Remediation - Project Update

Site Remediation System Design and Operations

- Soil vapor remediation efforts are ongoing since December 2022 to reduce contamination footprint.
- The remedial effort continues to decrease the area of concern. VP-2 the concentration was previously 210,000 μg/m3 and is currently 1,410 μg/m3.
- Estimate five additional years of soil vapor extraction to reduce concentrations below health risk screening levels.
- Quarterly progress reports are required by the lead oversight agency OCHCA.
- The lateral and vertical extent of VOCs, specifically PCE & TCE within soil vapor appear to be adequately defined.

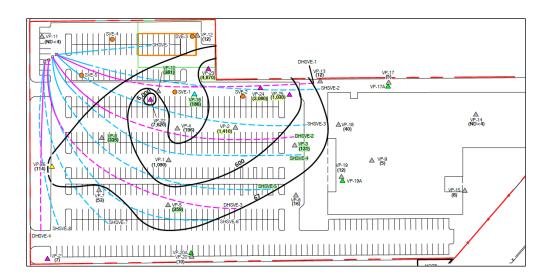



Current Capital Projects Orange Education Center Site Development Options

3 Viable Development Options:

- 1. Lease an Alternative Property
- 2. Purchase a New Property
- 3. Redevelop the Existing Site

Redevelopment Option:

- Implement Vapor Intrusion Mitigation Measures
 - Meeting environmental and safety regulations





Current Capital Projects Campus Entrance Improvements Phase 1 Santiago Canyon College

Project Summary:

- Project is a result of the Blaser Settlement to correct path of travel slope deficiencies in and around the quad adjacent several building locations, the front campus entrance and access from the public right of way and nearest bus stop, including areas around the fountain.
- Phase 1: construction of a new roundabout and drop off east of the Library, between parking lot 6 and the East Chapman entry, which is in alignment with the Campus Facility Master Plan.

Current Status:

- The Notice of Completion was approved by the Board of Trustees on August 12, 2024.
- Secondary projects:
 - Parking Lot 6 camera cabling is completed.
 - In close-out.
- \$5.5 million (under review)





Current Capital Projects Campus Entrance Improvements Phase 2 Santiago Canyon College

Project Summary:

- Project is a result of the Blaser Settlement to correct path of travel slope deficiencies in and around the quad adjacent several building locations, the front campus entrance and access from the public right of way and nearest bus stop, including areas around the fountain.
- Phase 2: path of travel improvements from main Chapman entrance west sidewalk up through Strenger Plaza, fountain improvements, and hardscape/landscape work adjacent Buildings D, E and Library.


Current Status:

- Project phasing aligned to fit current budget and college priorities
- Construction phase
- Excavation and site utilities

Budget:

\$9.1 million





Current Capital Projects Campus Entrance Improvements Phase 2 Santiago Canyon College





Current Capital Projects Campus Entrance Improvements Phase 2 Logistics Plan Vehicular Routes



Current Capital Projects Campus Entrance Improvements Phase 2 Logistics Plan Pedestrian Paths of Travel



Current Capital Projects Campus Entrance Improvements Phase 2 Logistics Plan Loading Zones





Current Capital Projects Santiago Canyon College

Project	Status	Estimated Budget
Soccer Path of Travel (POT) & Seating Repairs	The Notice of Completion was approved by the Board of Trustees on July 14, 2025. In close-out.	\$881,390





Current Capital Projects District Operations Center

Project	Status	Estimated Budget
Exterior Window Replacement	Award of bid for contractor services was approved by the Board of Trustees on August 11, 2025.	\$1,200,000



Scheduled Maintenance Projects



2022-2024 (SM23) Scheduled Maintenance Projects

State Allocation

- Allocation for Scheduled Maintenance and Instructional Equipment from the State was \$7,651,534. All funding will be allocated to Scheduled Maintenance only. The original allocation was \$18,882,875, a reduction of \$11,231,341 due to State budget reductions.
 - ▶ The allocation for 23/24 was \$128,753. The allocation is \$87,553 for SAC and \$41,200 for SCC. All funding for 23/24 is to be utilized for SM23 projects due to shortfall in budgets. Total SM23 allocation is \$7,780,287.

SAC	\$5,057,553
SCC	\$2,181,700
DO	_\$541,034
	\$7,780,287



2022-2024 (SM23) Scheduled Maintenance Santa Ana College Projects

Project	Status	Estimated Budget
CEC Improvements	Phase 1(Interior Improvements) has been completed. Phase 2 (Exterior Improvements & HVAC) is in the bid phase.	\$1,200,000
Fire Systems & Code Repairs (SAC, DMC, CEC & OCSRTA)	Construction phase. Construction continues at OCSRTA.	\$1,177,553
Bldg E Pool Equipment Replacement	Pre-construction phase. Construction is anticipated to start early September 2025.	\$700,000
Bldg E Pool Resurface	Pre-construction phase. Construction is anticipated to start early September 2025.	\$470,000
Bldg A Data Center HVAC Upgrade	Design phase.	\$500,000

2022-2024 (SM23) Scheduled Maintenance Santiago Canyon College Projects

Project	Status	Estimated Budget
Bldg T ADA Sidewalk Repairs	Project approved by DSA.	\$400,000
Fire Systems & Code Repairs	Close-out phase.	\$1,041,700
SC Air & Vacuum Systems	Construction phase.	\$335,700
Bldg D Entrance Auto Door Replacement	Bid phase.	\$60,000



2022-2024 (SM23) Scheduled Maintenance District Operations Center Projects

Project	Status	Estimated Budget
Plumbing Repairs	Design phase.	\$125,034
HVAC VAV Valve Replacement	Close-out phase.	\$300,000



2022-2024 (SM23) Completed Projects Santa Ana College

Project	Status	Expended Amount
CEC Roofing Repairs	Completed.	\$962,013
Fire Systems & Code Repairs	Completed.	\$8,745



2022-2024 (SM23) Completed Projects Santiago Canyon College

Project	Status	Expended Amount
Bldgs D, E, H & SC Lockset Repairs	Completed.	\$41,363
Bldg D HVAC	Completed.	\$117,101
Bldg G Mechanical Insulation Repairs	Completed.	\$39,089
Bldgs A & B Siding Repairs	Completed.	\$79,032



2021-2022 (SM22) Scheduled Maintenance Projects

State Allocation

- Allocation for Scheduled Maintenance and Instructional Equipment from the State was \$11,386,817. All funding will be allocated to Scheduled Maintenance only.
 - ► The allocation is \$7,284,610 for SAC, \$3,602,207 for SCC and DO \$500,000.

SAC	\$7,284,610
SCC	\$3,602,207
DO	<u>\$500,000</u>
	\$11,386,817



2021-2022 (SM22) Scheduled Maintenance Santa Ana College Projects

Project	Status	Estimated Budget
Building G HVAC Replacement	Bid phase.	\$1,992,831
Barrier Removal Campus-wide	Signage project is completed. Phase 2 will be an ADA path of travel improvement project in front of the CDC and is currently in the design phase.	\$200,000
DW Rekey SAC Phase 1	Door assessment at Santa Ana College is complete. Developing building key schedules.	\$756,000 (partially funded by DO SM22)



2021-2022 (SM22) Scheduled Maintenance Santa Ana College Projects

Project	Status	Estimated Budget
Buildings L, T, W & X HVAC & Roof Replacements	Close-out Phase.	\$2,700,323





2021-2022 (SM22) Completed Projects Santa Ana College

Project	Status	Expended Amount
Buildings F, I, & J Roof Replacement	Completed.	\$1,904,340
Bldg I and B10/B11 Roof	Completed.	\$232,513



2021-2022 (SM22) Completed Projects Santiago Canyon College

Project	Status	Expended Amount
A&B Plaza Entry	Completed.	\$109,020
Buildings A, B, D, G, H, SC Enclosure Repairs	Completed.	\$2,772,931
Building G Pool Repair	Completed.	\$454,748
Buildings A & B Air Handler	Completed.	\$156,401
CDC Repairs	Completed.	\$81,990



Facility Modification Requests



Facility Modification Requests Santa Ana College Projects

FMR #	Status	Estimated Budget
24-66 CEC E111 TV	College to proceed with procurement & installation of new TV. Will be removed from future updates.	N/A
24-68 Building S Security Doors	Received DSA approval. Bid phase.	\$336,920
24-78 OCSRTA AV Upgrades	In construction. Pending close-out.	\$398,000
24-113 Campus Safety Furniture	Construction commenced in August. Reception furniture and lockers to be installed in September.	\$59,900
24-118 VL205 PRIDE Center	In DSA review.	\$239,500
24-119 VL107 Reconfiguration	In DSA review.	\$171,500
24-149 Fine & Performing Arts Dust Collector	RFP for A/E services is being developed.	\$198,280
24-150 Fine & Performing Arts Projector & Screen Relocation	Structural review completed. SOLQ is being developed.	\$33,820
24-152 Fine & Performing Arts Lockers	RFP for A/E services is being developed.	\$147,128
25-42 S213 Reconfiguration	Schematic design approved by Executive Group. Design Development sign-off pending.	\$165,000
25-51 OCSRTA Storage Containers	College to proceed with procurement. Facilities to inspect installation.	N/A
25-60 Library Book Drop Box	College to proceed with installation. Will be removed from future updates.	N/A
25-67 Building T Elevator	RFP for A/E services is being developed.	\$767,500

Facility Modification Requests Santa Ana College Projects

FMR #	Status	Estimated Budget
25-68 OCSRTA Ground Swales	The agreement for architectural services is anticipated for approval by the Board of Trustees on 9/15/25.	\$485,000
25-87 MCHS New E-Sports Lab	ROE issued to SAUSD. Pending Form 3 approval from College.	\$21,200
25-94 E108 Computer Lab Upgrade	Pending Form 3 approval from College.	\$402,500
25-95 Kinesiology Branding	College to proceed. Licensed contractor and formal bid is required.	N/A




Current Capital Projects Campus Requested Santa Ana College

Project (Former FMR)	Status	Estimated Budget
3727 Building K Canopy	In DSA review.	\$1,053,925
3772 ITS Center Reconfiguration*	Design development phase.	\$3,900,000
3774 SAC Dunlap Amphitheater* Shade	Completed schematic design phase.	\$1,917,250
3775 SAC Central Mall Shade*	Completed schematic design phase.	\$372,167
3785 DMC Relocation*	The agreement for architectural services is anticipated for approval by the Board of Trustees on 9/15/25.	\$5,811,000
3787 Weight Rm. Windows/Field Railings	Design kickoff meeting scheduled.	\$825,075
3789 Building L Elevator Modernization	Design phase.	\$734,500
3790 Math Relocation and Reconfiguration*	RFP for architectural services underway. Paper screening completed on 8/22/25. Interviews scheduled for 9/5/25.	\$2,910,000
3794 SAC AV Upgrade	In DSA review.	\$848,000
3795 CEC AV Upgrade	In DSA review.	\$1,372,000
3798 New Synthetic Football Field	Construction phase.	\$6,540,058

^{*} Additional Project Detail on Following Slides

Facility Modification Request Updates September 3, 2025

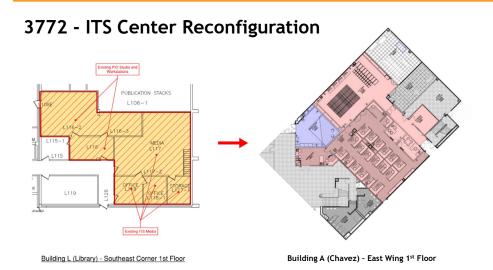

3785 - DMC Relocation PUBLISHON STACKS LINE-2 LINE

3790 - Math Dept. Relocation & Reconfiguration




SAC Moves / Relocations / Reconfigurations

Digital Media Center (DMC) - 1st Floor



Facility Modification Request Updates September 3, 2025

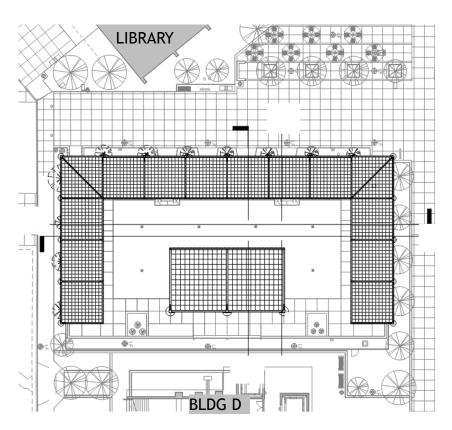




Dunlap Amphitheater





Facility Modification Request Updates September 3, 2025

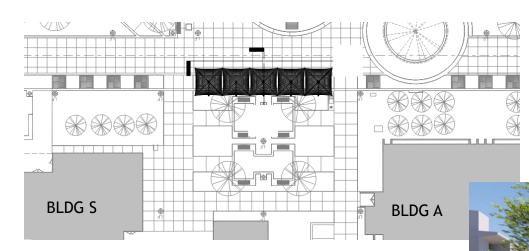

Central Mall Shade Structures





Patricianio (IIIIIII)

Facility Modification Requests Santiago Canyon College

FMR #	Status	Estimated Budget
25-13 Workstation Configuration	Working on Form 2 assessment.	TBD
25-31 SC Autoclave & Water Treatment Systems	Substantial completion as of 8/4/25. Board approval of Notice of Completion pending.	\$251,800
25-50 Bluebolt Solar Benches Lease	FMR has been canceled due to no response from Bluebolt about DSA requirement. Will be removed from future updates.	N/A
25-79 A209-B207 Projectors	College completed B207 installation and is postponing A209 installation. Will be removed from future updates.	N/A
25-86 H229 Projector	Working on Form 2 assessment.	TBD
26-01 D208 MESA Center Reconfiguration	Working on Form 2 assessment.	TBD
26-04 TV Installations	Working on Form 2 assessment.	TBD



Current Capital Projects Campus Requested Santiago Canyon College

Project (Former FMR)	Status	Estimated Budget
3807 Water Utility Sciences	Project kick-off meeting was held on 8/12/25.	\$3,764,363
3779 Jamboree Marquee	Project is on hold and will be removed from updates.	\$442,094



ADA Transition Plan & Blaser Settlement



ADA Transition Plan

Description/Scope: Removal of Barriers as outlined in the ADA Transition Plan.

Completed Activities as of June 2, 2025:

	ADA Transition Plan Progress				
Site		No. of Issues	Completed	Remaining	% Complete
SCC		2,937	1,424	1,513	48%
SAC		6,166	2,557	3,609	41%
DO		526	107	419	20%
Other		1,221	168	1,053	14%
	Total	10,850	4,256	6,594	39%



Blaser Settlement

Blaser Settlement deficiency items completed to date:

- ▶ 388 out of 417 exterior (93%) deficiencies have been corrected and 206 completed out of 241 items for interior (85%).
- Overall, the Blaser Settlement barrier corrective items are 90% complete.
- Multiple projects are currently in various phases of planning, design and construction.



Districtwide Access Control & Key Test Pilot Projects



Current Test Pilots Access Control & Key Projects Districtwide

Project	Status	Estimated Budget
SAC Building D	Received DSA approval in June 2023. Construction is currently unfunded.	\$1,626,855 (under review)
SAC CEC (mechanical re- key only)	Rekey to Medeco cylinders is completed. This project will be removed.	\$39,000 (expended amount)
SCC Buildings D & H	Received DSA approval in October 2023. Construction is currently unfunded.	\$3,225,787 (under review)
DW Rekey SAC Phase 1	Door assessment at Santa Ana College is complete. Developing building key schedules.	\$756,000 (partially funded by DO SM22)

Revisions to the AR 3501 are under review. Work Group meeting to be scheduled.



Districtwide Unfunded Projects



Districtwide Unfunded Projects

As of March 4, 2025:

- Five-Year Capital Construction Plan (Facility Master Plan 2026-2030): \$1.2 billion
- ► Five-Year Scheduled Maintenance Plan & Repair Work (w/ADA): \$231 million
- Fire Life Safety Repair Work: \$14 million
- Stormwater & Sustainability Projects: \$69.6 million
- Safety/Security Projects (e.g. Key and Access Control Infrastructure) \$104 million
- Districtwide Technology Infrastructure (e.g. ITS): \$20.6 million

Note: Projects may be listed on multiple categories due to the nature of the scope of work (e.g. infrastructure and technology)

RANCHO SANTIAGO
Community College District

State Chancellor's Office Deadlines



Districtwide Planning State Chancellor's Office Deadlines

2027-31 Five-Year Capital Outlay Plan was due July 1, 2025 - submitted

In Progress and currently working on:

- ▶ 2025-26 Space Inventory Report that is due October 6, 2025
- 2024-25 Energy Usage Data that is due December 1, 2025
- ▶ 2025-26 Five-Year Scheduled Maintenance Plan that is due October 27, 2025
- 2025-26 Instructional Support Equipment Five-Year Plan is due December 1, 2025



Real Estate and Capital Planning



Real Estate and Capital Planning

Santa Ana College

Working with Kosmont Realty evaluating best and highest use options for both Digital Media Center and Bristol & 17th Street properties. This includes assessing short-term, long-term leases, joint-occupancy as well as surplus of properties processes.

Santiago Canyon College

Working with Lee & Associates evaluating potential new lease spaces, best and highest use options (e.g. various leases) for the existing Batavia property, as well as evaluating new potential properties for acquisition.



Energy and Sustainability



Districtwide Planning Sustainability Master Plan Update

- ► The Sustainable RSCCD Committee completed its review of the 2015 Sustainability Master Plan goals and objectives and finalized its 2025 update.
- ▶ District presented the 2025 proposed plan to the BFC committee on May 20, 2025. The committee requested additional information which will be presented at a future meeting.
- ▶ Next Sustainable RSCCD Committee meeting is on September 17, 2025
- Link to view RSCCD 2025 Sustainability Plan: <u>Sustainable RSCCD Committee</u> (SRC)



District-Wide Planning Energy & Sustainability Update

Project	Status
California Energy Commission (CEC) Energy Benchmarking Annual Report	The 2024 energy benchmarking report was submitted to the CEC on April 21, 2025. This is an annual energy report that is required for any commercial buildings more than 50,000 sq ft. Received exemption approval for DMC site on July 28, 2025.
Sustainability Biennial Report	The Sustainability Biennial Report draft is nearly complete. Report will be shared in the next SRC meeting.
HVAC and Building Automation Optimization	Conducted first phase of assessments and recommendations. Continuing to review existing HVAC equipment and controls to look for optimal settings that will reduce our energy usage and preserve equipment longevity. Provided building automation training to M&O staff to maximize control usage and HVAC scheduling.

District-Wide Planning Energy & Sustainability Update

Project	Status
Energy Management Dashboard	Working on developing an interactive dashboard system that tracks utility performance and other metrics focused on sustainability areas. The District will present this dashboard to the SRC members at a future meeting.
SCC Microgrid Feasibility Assessment	Contract for engineering services for Microgrid Feasibility Assessment was approved by the Board of Trustees on August 11, 2025.
Stormwater Management Plan and Nonfunctional Turf Compliance Assessment	Currently drafting scope of work for districtwide assessment and other planning related to future compliance with AB1572 for non-functional turf potable water irrigation.



District-Wide Planning Energy & Sustainability Update

Project	Status
Sustainability Field Trip	The Sustainability Resource Committee completed their second field trip this year to the SoCal Gas Hydrogen Microgrid System. The tour provided valuable insights into the technology and practical use of hydrogen within a microgrid setup.





Physical Resources Committee Meeting September 3, 2025

Questions

